


EARLY WARNING SYSTEM (BLOWOUT)

MINE POOL RESPONSE BY DISCHARGING AT PRIMARY DRAIN

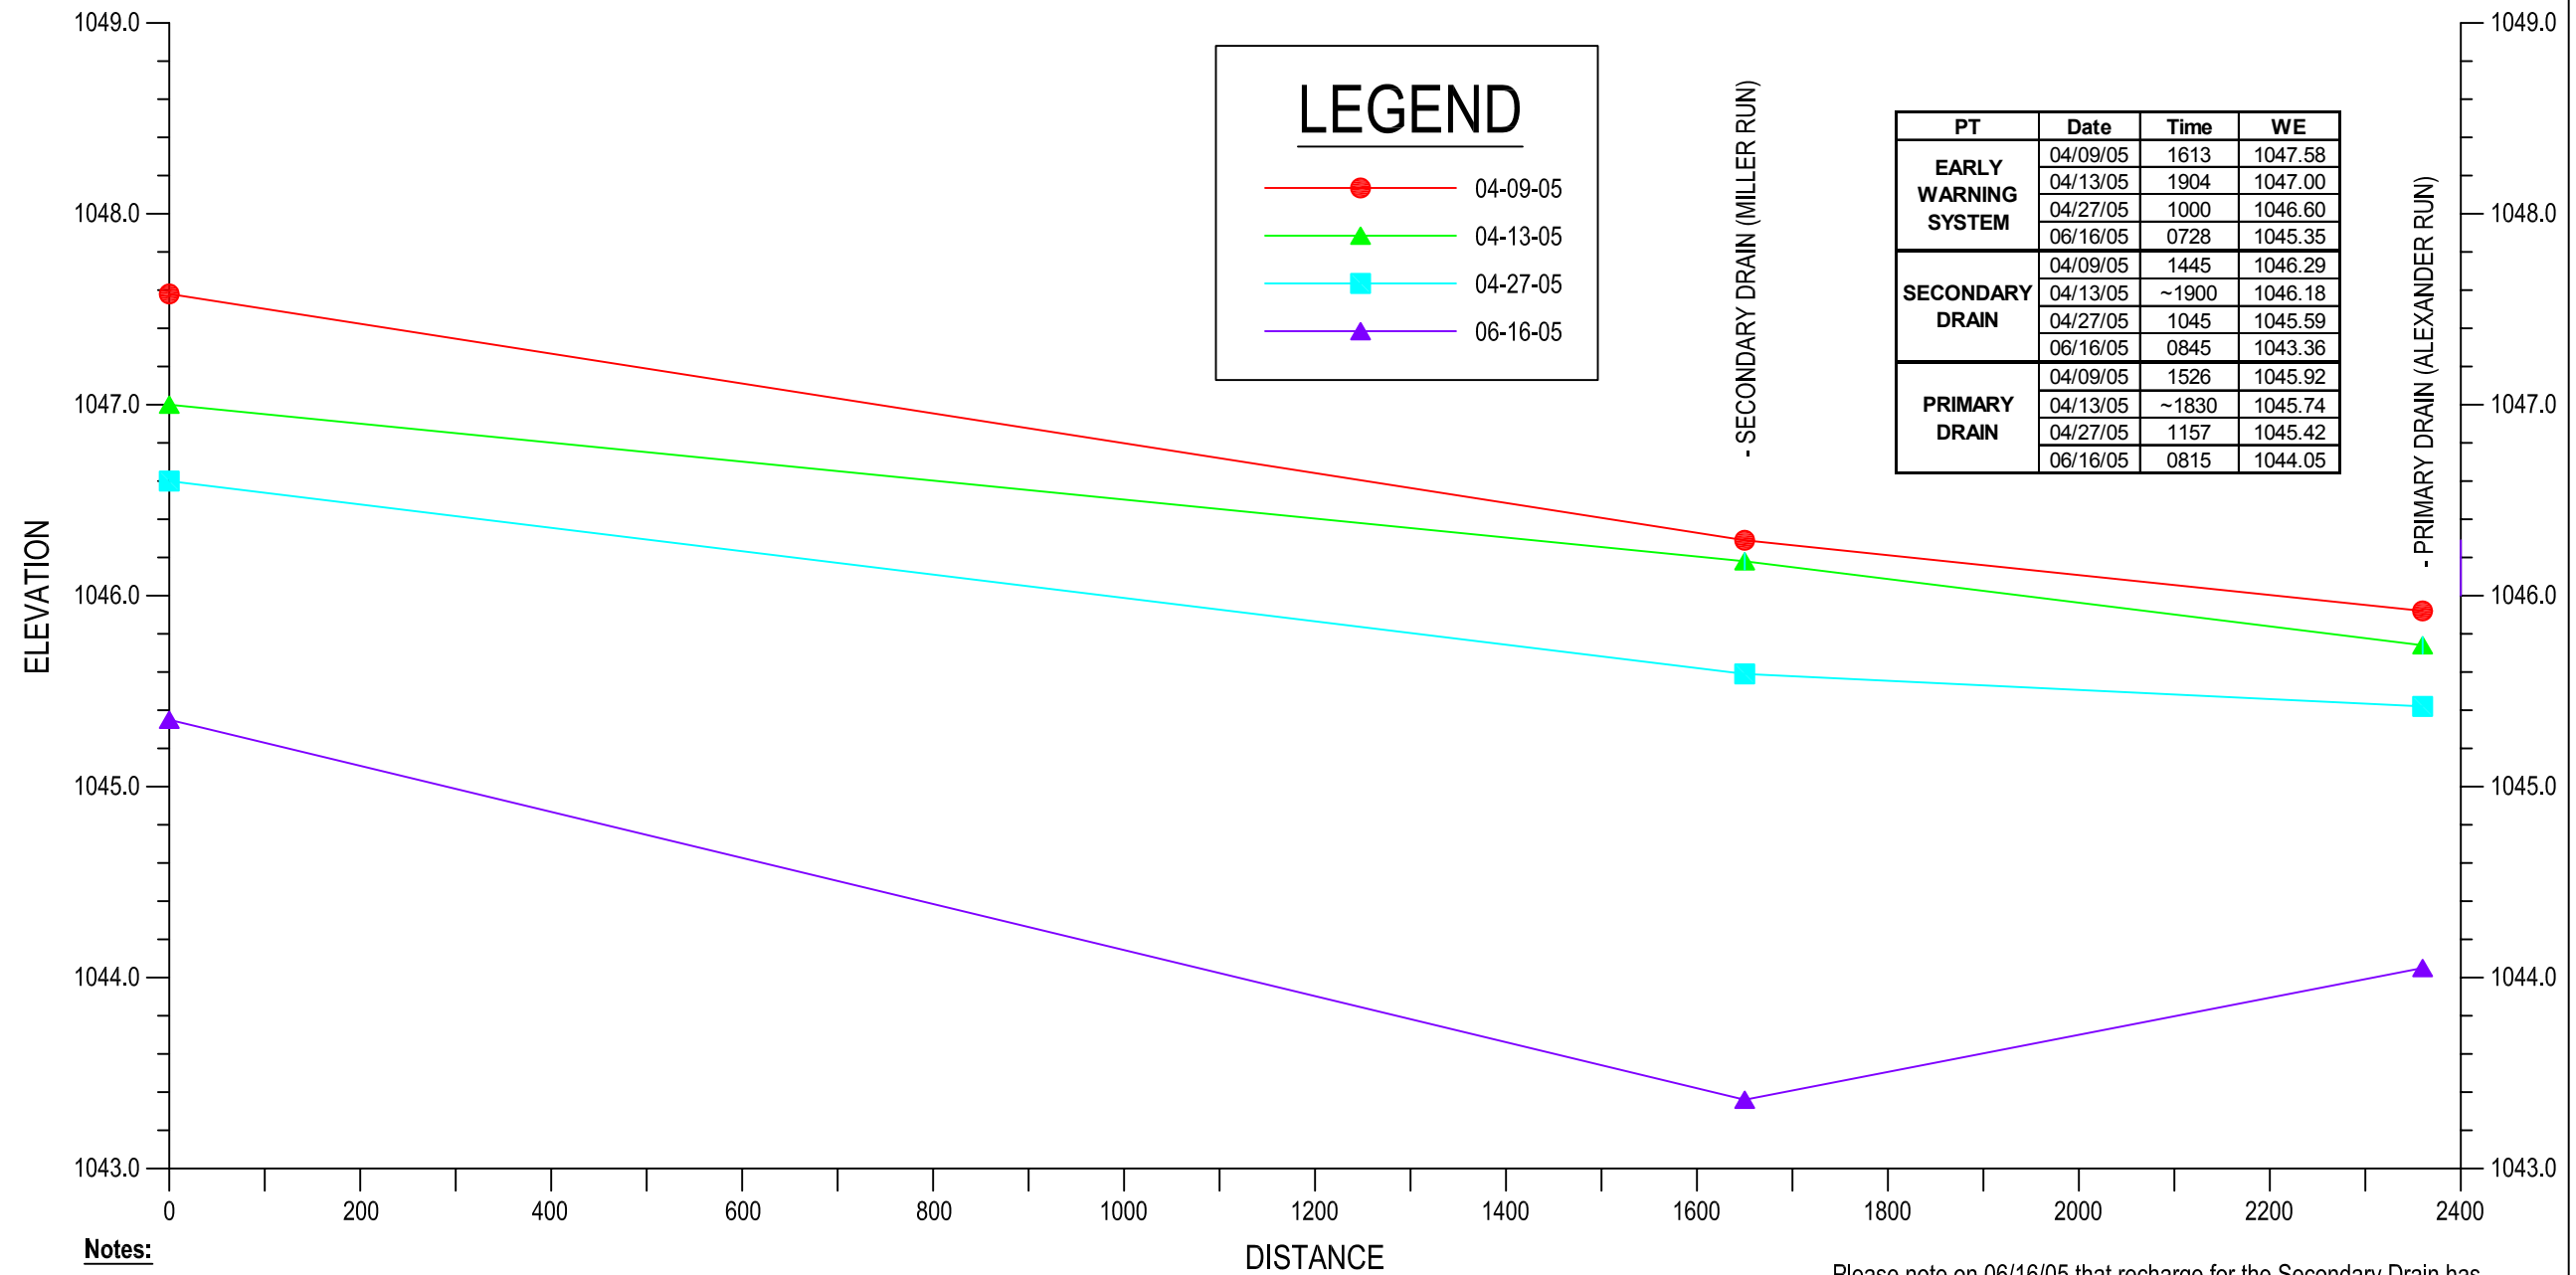

Notes:

EARLY WARNING SYSTEM (Blowout): pumping suspended 04/08/05 @ 1630; 05/09/05 installed.
 SECONDARY DRAIN (Test Pit 3): excavated 04/08/05; no drainage; 04/13/05 riser installed; 05/09/05 completed.
 PRIMARY DRAIN (Test Pit 1): excavated 04/08/05; 6" pump operational from 04/09/05 @ 0854 to 04/10/05 @ 1357; temporary gravity drain online 04/10/05 @ 1357 to 05/20/05 @ ~1700; Permanent gravity drain function from 5/20/05 @ ~1700 to date.

Please note on 06/16/05 that recharge for the Secondary Drain has been significantly reduced by the impact of the Primary Drain "test weir". The crest of the permanent weir has since been raised to the design elevation of 1044.5'.
